

Defense Acquisition in Transition 8th Annual Symposium

Acquisition Risks in a World of Joint Capabilities

Mary Maureen Brown University of North Carolina at Charlotte

Robert Kravchuk University of North Carolina at Charlotte

Graham Owen
University of North Carolina at Charlotte



This material is based upon work supported by the Naval Postgraduate School Acquisition Research Program under Grant No. N00244-11-1-0019

maintaining the data needed, and c including suggestions for reducing	lection of information is estimated to ompleting and reviewing the collecti this burden, to Washington Headqua uld be aware that notwithstanding an DMB control number.	on of information. Send comments arters Services, Directorate for Info	regarding this burden estimate or formation Operations and Reports	or any other aspect of the 1215 Jefferson Davis	is collection of information, Highway, Suite 1204, Arlington		
1. REPORT DATE MAY 2011	2. REPORT TYPE			3. DATES COVERED 00-00-2011 to 00-00-2011			
4. TITLE AND SUBTITLE					5a. CONTRACT NUMBER		
Acquisition Risks in a World of Joint Capabilities					5b. GRANT NUMBER		
					5c. PROGRAM ELEMENT NUMBER		
6. AUTHOR(S)					5d. PROJECT NUMBER		
					5e. TASK NUMBER		
				5f. WORK UNIT NUMBER			
7. PERFORMING ORGANIZATION NAME(S) AND ADDRESS(ES) University of North Carolina at Charlotte,9201 University City Blvd,Charlotte,NC,28223-0001					8. PERFORMING ORGANIZATION REPORT NUMBER		
9. SPONSORING/MONITORING AGENCY NAME(S) AND ADDRESS(ES)					10. SPONSOR/MONITOR'S ACRONYM(S)		
					11. SPONSOR/MONITOR'S REPORT NUMBER(S)		
12. DISTRIBUTION/AVAII Approved for publ	ABILITY STATEMENT ic release; distributi	on unlimited					
	otes aval Postgraduate So U.S. Government of		-	arch Sympos	ium, 10-12 May		
14. ABSTRACT							
15. SUBJECT TERMS							
16. SECURITY CLASSIFIC	ATION OF:	17. LIMITATION OF	18. NUMBER	19a. NAME OF			
a. REPORT unclassified	b. ABSTRACT unclassified	c. THIS PAGE unclassified	Same as Report (SAR)	OF PAGES 20	RESPONSIBLE PERSON		

Report Documentation Page

Form Approved OMB No. 0704-0188



Purpose

examines the

Despite the most intense management efforts of the best-trained, best-qualified acquisition professionals; despite vigorous acquisition reform, oversight, and scrutiny, cost over runs and schedule delays

of technological developments

remains unacceptably high.

funding and data interdependencies that exist among MDAPs to determine if it roblems ma be due to the interdependent nature of joint capabilities.



Joint Capabilities

Join Capabilities and Network Centric Warfare

is an emerging theory of war based on the concepts of nonlinearity, com_lexit_ and chaos. It is less deterministic and more emergent; it has less focus on the physical than the behavioral;

and it has less focus on things than on relationships

ADM Cebrowski



Complexity and Joint Capabilities



Nonlinear interaction

Combat forces composed of a large number of nonlinearly interacting parts

Decentralized Control

There is no master "oracle" dictating the actions of each and every combatant

Self-Organization

Local action, which often appears "chaotic," induces long-range order

Non-equilibrium Order

Military conflicts, by their nature, proceed far from equilibrium. Correlation of local effects is key

Adaptation

Combat forces must continually adapt and coevolve in a changing environment

Collectivist Dynamics

There is a continual feedback between the behavior of combatants and the command structure

-- Moffat



Vulnerabilities

- Incomplete Information
- Incomplete Payoff Structures
- Inability to Isolate Cause and Effect
- Unknown Response Options
- Multiple and Conflicting

Representations of Environmental variety

- Perturbations
- Multiple Constraints

Cost Overruns

Schedule Delays

Feature Shortfalls



Research Objectives

Applied Research :: 2011

- Identify and characterize the nature of MDAP interdependencies.
- Test to see if performance breaches (specifically, feature changes, cost overruns, and budget shortfalls) correlate with any of the interdependency characteristics.
- Isolate the extent to which acquisition performance breaches (i.e. per unit cost growth, schedule delays, and feature shortfalls) in an u_stream_ro_ram cascade to downstream interde_endent MDAP programs.
- Compute overall annual MDAP network metrics of complexity dating back to 2005 to see how they might relate to the total acquisition spending.



Labor

DAES

Information

Interdependency Dimensions & Data

Damir

ResourceDirectionCharacteristics✓ FinancialPooled✓ Joint✓ Data✓ Sequential✓ Stage✓ AuthorityReciprocal✓ Turnover

RDOCs






Data Interdependencies

Growing Interdependencies and Growing Complexity

97 Nodes


353 Links

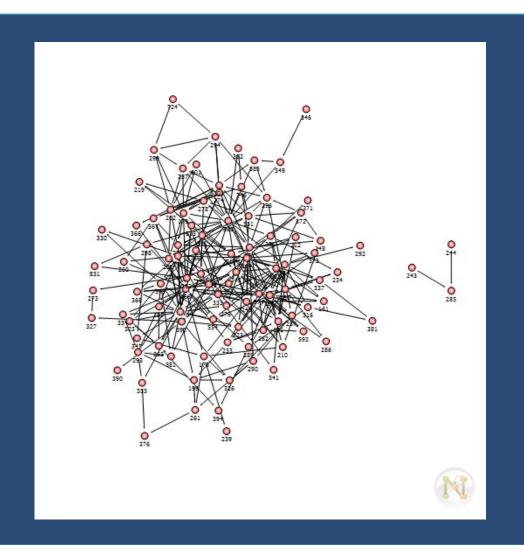



Fiscal Year 2004


39 Links

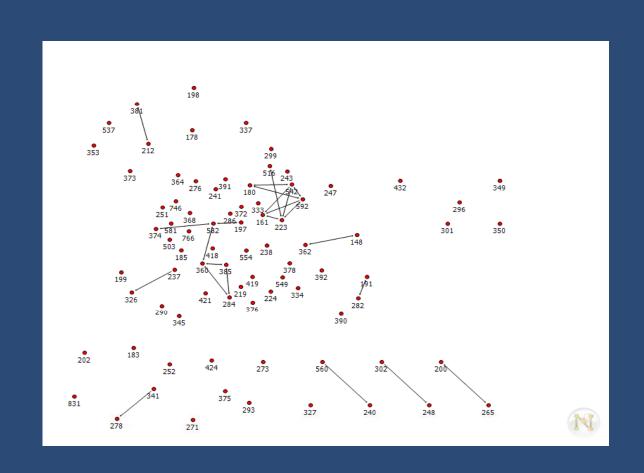



Fiscal Year 2005


64 Links

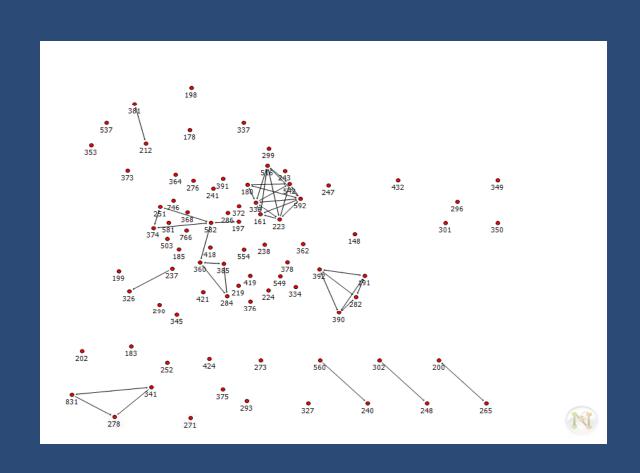



Fiscal Year 2006


87 Links

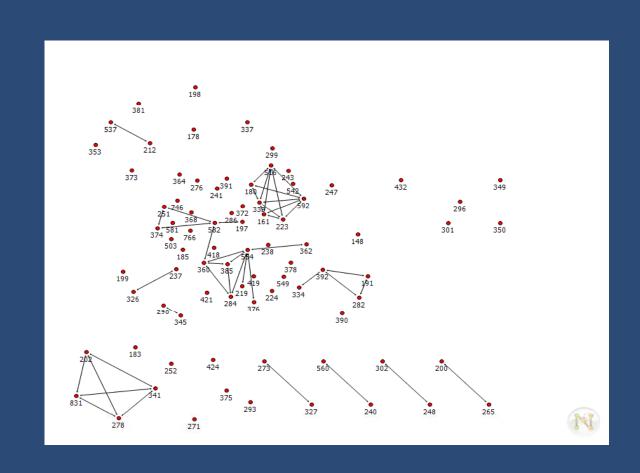



Fiscal Year 2007


152 Links

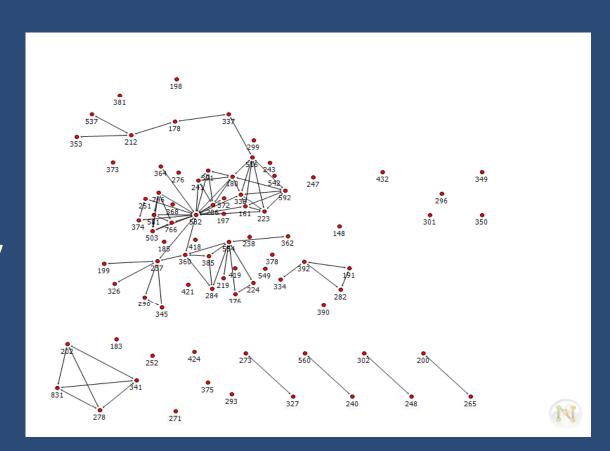



Fiscal Year 2009


291 Links

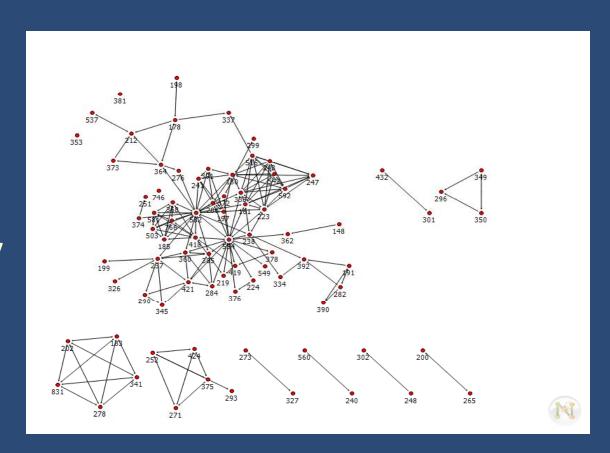



Funding Interdependencies


Percent of MDAPs that Share a Funding Account

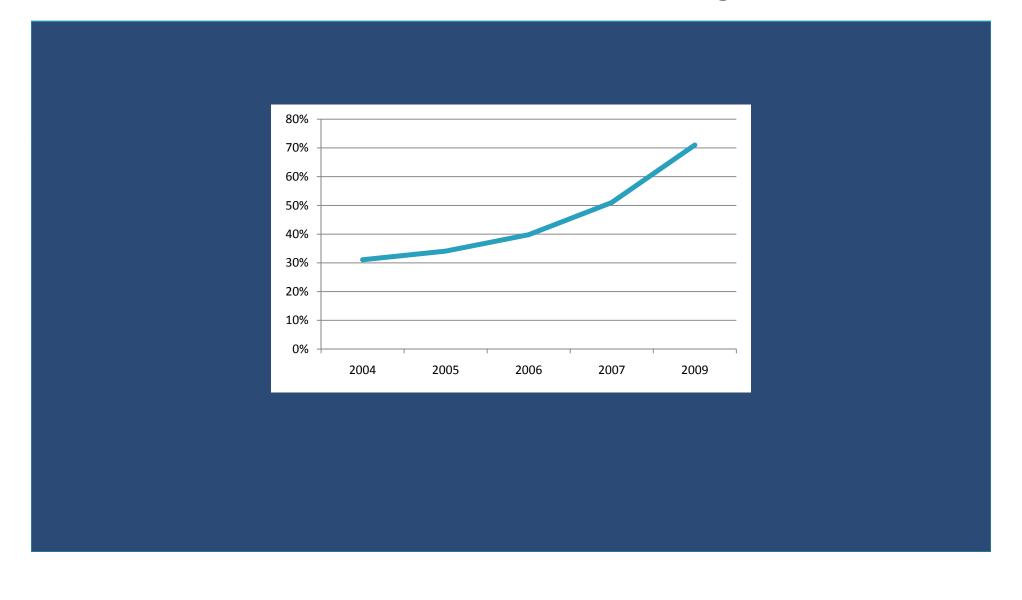




Scale Free Networks

Number of MDAPs

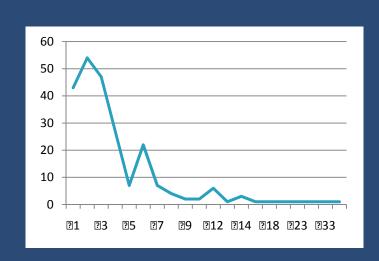

Number of Funding Links

Number of MDAPs




Number of Data Links



Data & Funding Interdependencies

Percent of MDAPs that Share Both Data & Funding Interdependencies

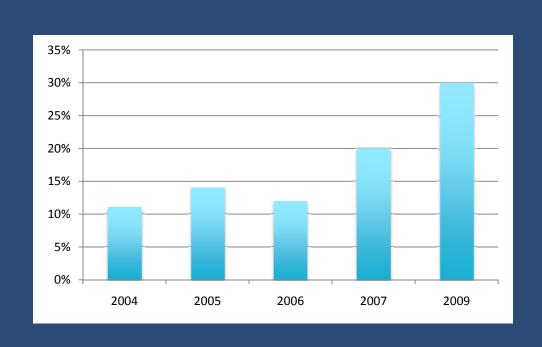



Regression Models

Data Links →
Schedule Cost Variance

Data and Funding Links ->
APB Performance Breaches

Joint Status →
Pct Growth from Baseline

Summary of Regression Findings*								
	Pct Growth From Baseline	RDT&E PAUC Pct Growth	APB Perf Breaches	Schedule Cost Variance	Estimation Cost Variance	Engineering Cost Variance		
Number of Program Elements								
Total Number of Signatures				-				
Number of Data Links				+				
Joint Status	+							
Both Data and Funding Links		1	+					
Funding Links Only	-							
*Controlling for Development Estimate, Turnover, Stage								

*Controlling for Development Estimate, Turnover, Stage



First & Second Order Cascades

Summary of First Order Cascades

- + = Positive Cascade
- = Negative Cascade
- x = Positive Cascade for MDAPs that experience Greater than 13% Growth
- z = Negative Cascade for MDAPs that experience Greater than 13% Growth

Year	Pct Growth From Baseline	RDT&E PAUC Pct Growth	APB Perf Breaches	Schedule Cost Variance	Estimation Cost Variance	Engineering Cost Variance			
	Funding Interdependencies								
2005									
2006	+			+					
2007	+	+	+ X	x					
2009	+	+ X	-	-	-	-			
Data Interdependencies									
2006	x	X		-		- z			
2007	X	+ X	+			+			
2009	X	X	+	-	- Z	- Z			
	Both Data and Funding Interdependencies								
2006					-	+			
2007			-						
2009	Х	X			+				

Second Order:

PAUC Pct Growth

>13 PAUC Pct Growth

>13 Pct Growth From Baseline



Take Aways

1. Growth in Complexity

2. Data & Funding Networks are Scale Free

Data Links → Schedule Cost Variance

3. Regressions

Data and Funding Links → APB Performance Breaches

<u>Data Links</u> <u>Funding Links</u>

4. Cascades RDT&E PAUC Pct Growth RDT&E PAUC Pct Growth

APB Perf Breaches Pct Growth From Baseline

Engineering Cost Variance

5. Tipping Point Pct PAUC Growth

Pct Growth From Baseline



Next Steps

✓ Incorporate 2010 Data

✓ Test the Influence of Dyadic Analysis as a Measurement Tool

✓ Test the Influence of Structural Equation Modeling as a Measurement Tool
